ID	Task Name	Start	Finish	Late Start	Late Finish	Free Slack	Total Slack
1	CRITICAL PATH	Thu 4/1/04	Thu 5/27/04	Thu 4/1/04	Thu 5/27/04	0 days	0 days
2	ADMINISTRATIVE TASKS	Thu 4/1/04	Fri 4/2/04	Thu 4/1/04	Tue 4/6/04	0 days	0 days
3	Start Order	Thu 4/1/04	Thu 4/1/04	Thu 4/1/04	Thu 4/1/04	0 days	0 days
4	Building Permit	Fri 4/2/04	Fri 4/2/04	Fri 4/2/04	Fri 4/2/04	0 days	0 days
5	Soil Density Analysis	Fri 4/2/04	Fri 4/2/04	Tue 4/6/04	Tue 4/6/04	0 days	2 days
6	FOUNDATION(STAGE I)	Mon 4/5/04	Thu 4/15/04	Mon 4/5/04	Thu 4/22/04	0 days	0 days
7	Stake Foundation	Mon 4/5/04	Mon 4/5/04	Wed 4/7/04	Wed 4/7/04	2 days	2 days
8	Sewer & Water	Mon 4/5/04	Wed 4/7/04	Mon 4/5/04	Wed 4/7/04	0 days	0 days
9	Layout	Thu 4/8/04	Thu 4/8/04	Thu 4/8/04	Thu 4/8/04	0 days	0 days
10	Excavate	Thu 4/8/04	Thu 4/8/04	Thu 4/8/04	Thu 4/8/04	0 days	0 days
11	DOH Inspect	Fri 4/9/04	Fri 4/9/04	Fri 4/9/04	Fri 4/9/04	0 days	0 days
12	Stone & Set Foundation	Mon 4/12/04	Mon 4/12/04	Mon 4/12/04	Mon 4/12/04	0 days	0 days
13	Slab Plumbing	Tue 4/13/04	Tue 4/13/04	Tue 4/13/04	Tue 4/13/04	0 days	0 days
14	Grade & Pour Slab	Wed 4/14/04	Wed 4/14/04	Wed 4/14/04	Wed 4/14/04	0 days	0 days
15	Install Gas Meter	Thu 4/15/04	Thu 4/15/04	Thu 4/22/04	Thu 4/22/04	5 days	5 days
16	DOH Inspect	Thu 4/15/04	Thu 4/15/04	Thu 4/15/04	Thu 4/15/04	0 days	0 days
17	FRAMING(STAGE II)	Fri 4/16/04	Wed 4/28/04	Fri 4/16/04	Wed 5/19/04	0 days	0 days
18	Panel Delivery & Set	Fri 4/16/04	Mon 4/19/04	Fri 4/16/04	Mon 4/19/04	0 days	0 days
19	Roof Set	Tue 4/20/04	Tue 4/20/04	Tue 4/20/04	Tue 4/20/04	0 days	0 days
20	Shingles	Tue 4/20/04	Tue 4/20/04	Tue 4/20/04	Tue 4/20/04	0 days	0 days
21	Window Installation	Wed 4/21/04	Wed 4/21/04	Fri 4/23/04	Fri 4/23/04	0 days	2 days
22	Siding	Thu 4/22/04	Mon 4/26/04	Mon 4/26/04	Wed 4/28/04	0 days	2 days
23	Brick Install	Tue 4/27/04	Wed 4/28/04	Tue 5/18/04	Wed 5/19/04	0 days	15 days
24	Gutters & Downspouts	Tue 4/27/04	Tue 4/27/04	Wed 5/19/04	Wed 5/19/04	1 day	16 days
25	MECHANICALS	Wed 4/21/04	Thu 4/29/04	Wed 4/21/04	Thu 4/29/04	0 days	0 days
26	Electrical Service Panel	Wed 4/21/04	Wed 4/21/04	Wed 4/21/04	Wed 4/21/04	0 days	0 days
27	Install Electric Meter	Thu 4/22/04	Thu 4/22/04	Thu 4/22/04	Thu 4/22/04	0 days	0 days
28	Plumbing Rough	Fri 4/23/04	Fri 4/23/04	Fri 4/23/04	Fri 4/23/04	0 days	0 days
29	HVAC Rough	Mon 4/26/04	Mon 4/26/04	Mon 4/26/04	Mon 4/26/04	0 days	0 days
30	Electric Rough	Tue 4/27/04	Tue 4/27/04	Tue 4/27/04	Tue 4/27/04	0 days	0 days
31	Energy Technician	Wed 4/28/04	Wed 4/28/04	Wed 4/28/04	Wed 4/28/04	0 days	0 days
32	Insulation	Thu 4/29/04	Thu 4/29/04	Thu 4/29/04	Thu 4/29/04	0 days	0 days
33	DOH Inspect	Thu 4/29/04	Thu 4/29/04	Thu 4/29/04	Thu 4/29/04	0 days	0 days
34	DRYWALL(STAGE III)	Thu 4/29/04	Wed 5/12/04	Thu 4/29/04	Wed 5/12/04	0 days	0 days
35	Drywall Stock	Thu 4/29/04	Thu 4/29/04	Thu 4/29/04	Thu 4/29/04	0 days	0 days
36	Drywall	Fri 4/30/04	Tue 5/11/04	Fri 4/30/04	Tue 5/11/04	0 days	0 days
37	Drywall Spray	Wed 5/12/04	Wed 5/12/04	Wed 5/12/04	Wed 5/12/04	0 days	0 days
38	EXTERIOR	Thu 4/29/04	Fri 5/7/04	Thu 5/13/04	Thu 5/20/04	9 days	9 days
39	Paint Exterior	Thu 4/29/04	Thu 4/29/04	Thu 5/20/04	Thu 5/20/04	15 days	15 days
40	Exterior Flatwork	Fri 4/30/04	Mon 5/3/04	Thu 5/13/04	Fri 5/14/04	0 days	9 days
41	Detached Structures	Tue 5/4/04	Tue 5/4/04	Mon 5/17/04	Mon 5/17/04	0 days	9 days
42	Final Grade	Wed 5/5/04	Wed 5/5/04	Tue 5/18/04	Tue 5/18/04	0 days	9 days
43	Fence	Thu 5/6/04	Thu 5/6/04	Wed 5/19/04	Wed 5/19/04	0 days	9 days
44	Landscape	Fri 5/7/04	Fri 5/7/04	Thu 5/20/04	Thu 5/20/04	0 days	9 days
45	TRIM(STAGE IV)	Thu 5/13/04	Thu 5/27/04	Thu 5/13/04	Thu 5/27/04	0 days	0 days
46	Tile Floors	Thu 5/13/04	Thu 5/13/04	Thu 5/13/04	Thu 5/13/04	0 days	0 days
47	Cabinets	Thu 5/13/04	Thu 5/13/04	Fri 5/14/04	Fri 5/14/04	1 day	1 day
48	Cultured Marble Tops	Thu 5/13/04	Thu 5/13/04	Fri 5/14/04	Fri 5/14/04	1 day	1 day
49	Laminate Tops	Thu 5/13/04	Thu 5/13/04	Fri 5/14/04	Fri 5/14/04	1 day	1 day
50	Electric Trim	Fri 5/14/04	Fri 5/14/04	Fri 5/14/04	Fri 5/14/04	0 days	0 days
51	Light Fixtures	Fri 5/14/04	Fri 5/14/04	Mon 5/17/04	Mon 5/17/04	0 days	0 days
52	Carpentry Trim/Blinds	Mon 5/17/04	Tue 5/18/04	Mon 5/17/04	Tue 5/18/04	0 days	0 days
53	Plumbing Trim	Wed 5/19/04	Wed 5/19/04	Wed 5/19/04	Wed 5/19/04	0 days	0 days
54	Shelving	Thu 5/20/04	Thu 5/20/04	Thu 5/20/04	Thu 5/20/04	0 days	0 days
55	Mirrors	Thu 5/20/04	Thu 5/20/04	Thu 5/20/04	Thu 5/20/04	0 days	0 days
56	Carpet Sweep	Thu 5/20/04	Thu 5/20/04	Fri 5/21/04	Fri 5/21/04	1 day	1 day
57	DOH Inspection	Fri 5/21/04	Fri 5/21/04	Fri 5/21/04	Fri 5/21/04	0 days	0 days
58	Carpet Install	Mon 5/24/04	Mon 5/24/04	Mon 5/24/04	Mon 5/24/04	0 days	0 days
59	Alarm System	Mon 5/24/04	Mon 5/24/04	Mon 5/24/04	Mon 5/24/04	0 days	0 days
60	Paint Touch Up	Tue 5/25/04	Tue 5/25/04	Tue 5/25/04	Tue 5/25/04	0 days	0 days
61	Appliances	Tue 5/25/04	Tue 5/25/04	Tue 5/25/04	Tue 5/25/04	0 days	0 days
62	Final Clean	Wed 5/26/04	Wed 5/26/04	Wed 5/26/04	Wed 5/26/04	0 days	0 days
63	Set A/C	Thu 5/27/04	Thu 5/27/04	Thu 5/27/04	Thu 5/27/04	0 days	0 days
64	HOME INSPECTIONS	Thu 5/27/04	Thu 5/27/04	Thu 5/27/04	Thu 5/27/04	0 days	0 days
65	New Home Inspection	Thu 5/27/04	Thu 5/27/04	Thu 5/27/04	Thu 5/27/04	0 days	0 days
66	CLOSING	Thu 5/27/04	Thu 5/27/04	Thu 5/27/04	Thu 5/27/04	0 days	0 days

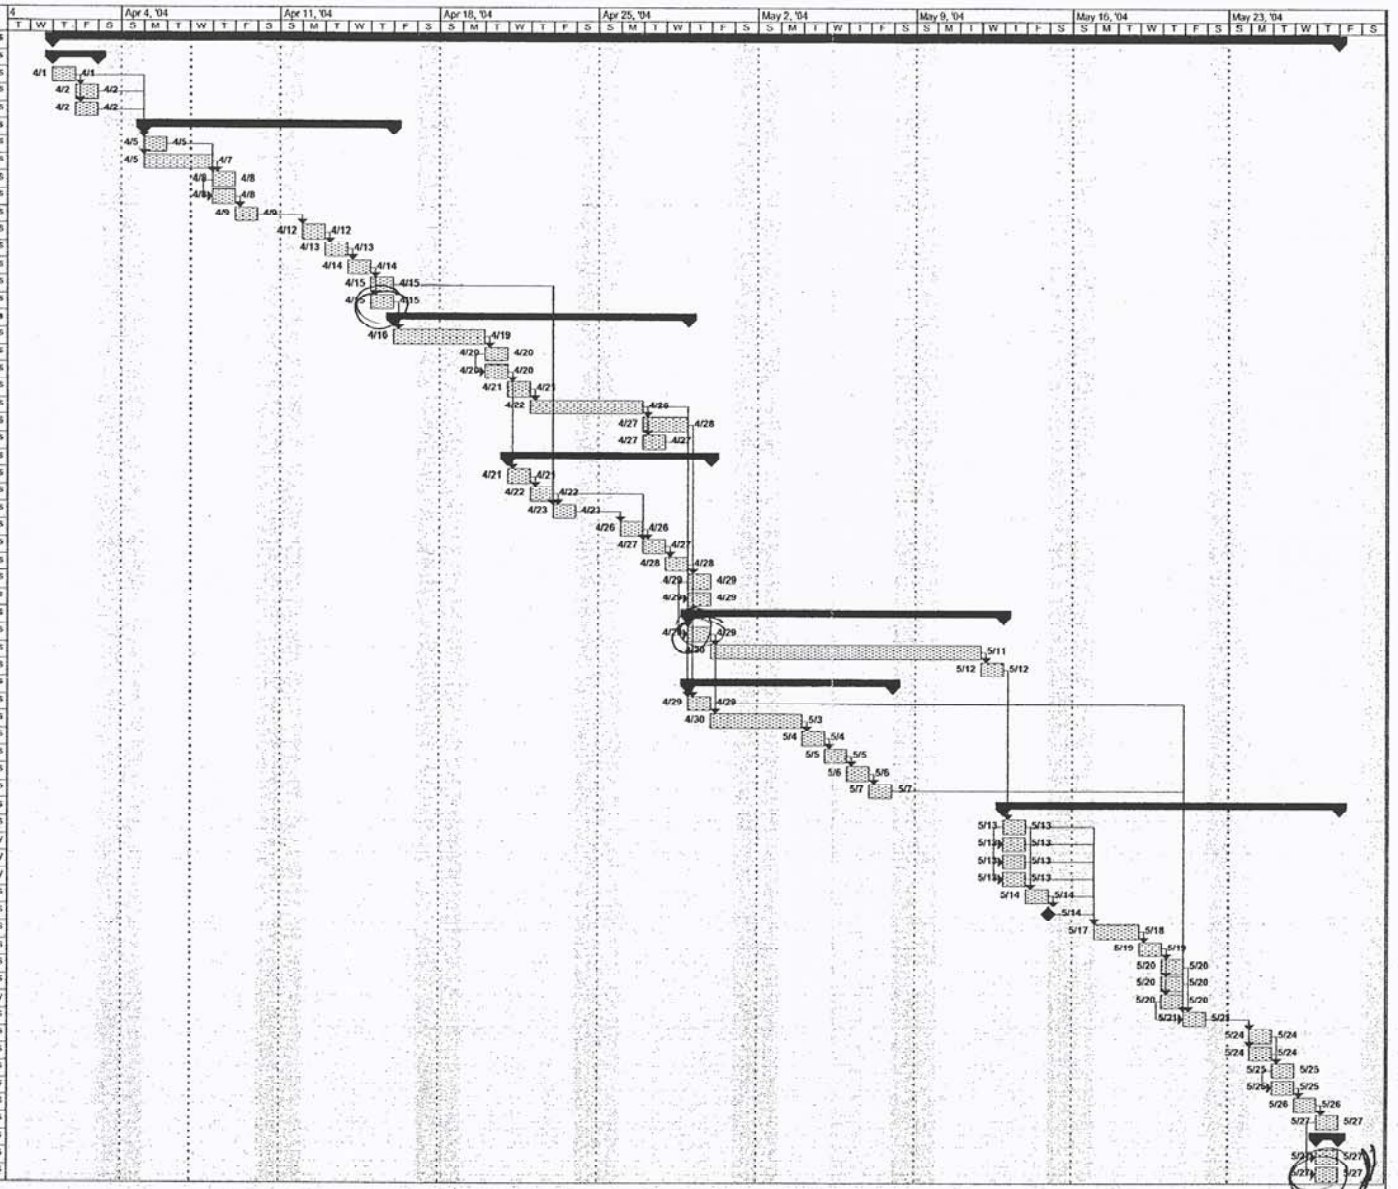

Project: Slab Master
Date: Wed 4/7/04

Task
Critical Task
Progress
Milestone
Summary
Rolled Up Task
Rolled Up Critical Task
Rolled Up Milestone
Rolled Up Progress
Split
External Tasks
Project Summary
Group By Summary
